

SEDIMENT CONTROL NOTES

- 1. A minimum of 48 hours notice must be given to the HOWARD COUNTY DEPARTMENT OF INSPECTIONS, LICENSING AND PERMITS, SEDIMENT CONTROL DIVISION PRIOR TO THE START OF ANY CONSTRUCTION (10:30 AM).

- 2. ALL VEGETATION AND STRUCTURAL PRACTICES ARE TO BE INSTALLED ACCORDING TO THE PROVISIONS OF THIS PLAN AND ARE TO BE IN CONFORMANCE WITH THE MOST CURRENT MARYLAND STANDARDS AND SPECIFICATIONS FOR SOIL EROSION AND SEDIMENT CONTROL AND REVISIONS THEREOF.

- 3. FOLLOWING INITIAL SOIL DISTURBANCE OR RE-EXPOSURE, PERMANENT OR TEMPORARY STABILIZATION SHALL BE INSTALLED WITHIN 48 HOURS.









- 4. ALL SEDIMENT TRANSDUCERS SHOWN MUST BE MANUAL AND WARNING SIGNS POSTED AROUND THESE POINTS IN ACCORDANCE WITH VOL. 1, CHAPTER 12, OF THE HOWARD COUNTY DESIGN MANUAL, STORM DRAINAGE.

- 5. ALL DISTURBED AREAS MUST BE STABILIZED WITHIN THE TIME PERIOD SPECIFIED ABOVE IN ACCORDANCE WITH THE MOST CURRENT STANDARDS AND SPECIFICATIONS FOR SOIL EROSION AND SEDIMENT CONTROL FOR PERMANENT SEEDING (SEC. 20.100) OR TEMPORARY SEEDING (SEC. 20.100) AND MAINTENANCE (SEC. 20.100) TEMPORARY STABILIZATION WITH MULCH ALONE CAN ONLY BE USED WHEN RECONSTRUCTED SEEDING DATES DO NOT ALLOW FOR PROPER CONSTRUCTION AND ESTABLISHMENT OF GRASSES.

- 6. ALL SEDIMENT CONTROL STRUCTURES ARE TO REMAIN IN PLACE AND ARE TO BE MAINTAINED IN OPERATIVE CONDITION UNTIL PERMISSION FOR THEIR REMOVAL HAS BEEN OBTAINED FROM THE HOWARD COUNTY SEDIMENT CONTROL INSPECTOR.

- 7. SITE ANALYSIS: TOTAL AREA OF SITE: 2.3060 ACRES; AREA TO BE REGRADED OR PAVED: 0.0265 ACRES; AREA TO BE VEGETATIVELY STABILIZED: 0.0265 ACRES; TOTAL CUT: 0.0530 CU. YDS.; TOTAL FILL: 0.0530 CU. YDS.; DISTRICT WASTE/ROOFDRAIN AREA LOCATION: SEE PLAN; ANY SEDIMENT CONTROL PRACTICE WHICH IS OBTAINED BY GRADING ACTIVITY FOR PLACEMENT OF UTILITIES MUST BE REPAIRED ON THE SAME DAY OF DISTURBANCE.























- 8. ADDITIONAL SEDIMENT CONTROLS MUST BE PROVIDED, IF DEMAND APPROVED BY THE HOWARD COUNTY SEDIMENT CONTROL INSPECTOR, ON ALL SITES WITH DISTURBED AREAS IN EXCESS OF THE PERCENT APPROVAL OF THE HOWARD COUNTY SHALL BE REQUESTED UPON COMPLETION OF INSTALLATION OF PERMANENT AND TEMPORARY SEDIMENT CONTROLS, BUT BEFORE PROCEEDING WITH ANY OTHER EARTH DISTURBANCE OR GRADING. OTHER BUILDING OR GRADING INSPECTION APPROVALS MAY NOT BE WITHHELD UNTIL THIS NATURAL APPROVAL.

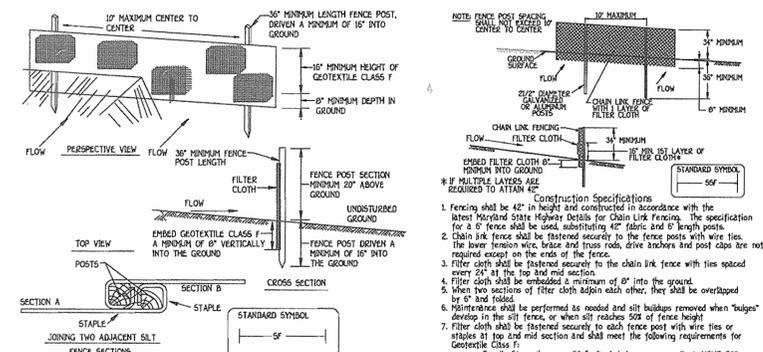

SCHEDULE A PERIMETER LANDSCAPE EDGE table with columns for P-1 ADJACENT TO ROADWAYS, P-2 ADJACENT TO PROPERTY PROPERTIES, P-3 ADJACENT TO PROPERTY PROPERTIES, and P-4 ADJACENT TO PROPERTY PROPERTIES.

CONSTRUCTION SPECIFICATIONS: 1. Fencing shall be 42" in height and constructed in accordance with the latest Maryland State Highway Details for Chain Link Fencing.

Table with columns for Slope, Slope Steepness, and Slope Length, detailing requirements for different slope conditions.

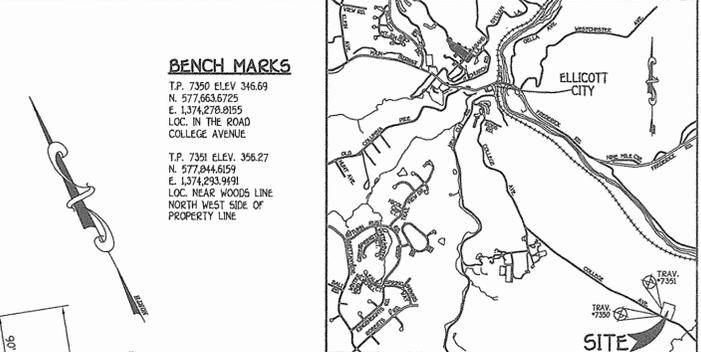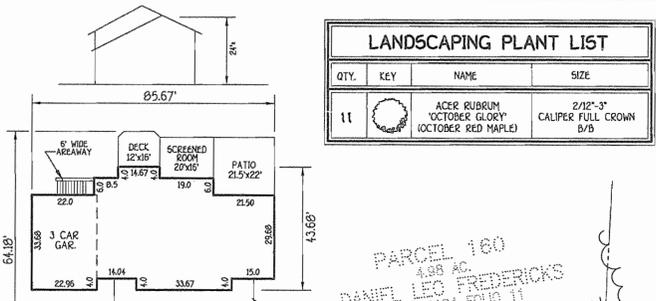

ADDRESS CHART table with columns for LOT NO., ADDRESS, and REVISION.

LEGEND table with columns for SYMBOL, DESCRIPTION, and REVISION.

LEGEND table with columns for SYMBOL, DESCRIPTION, and REVISION.

LEGEND table with columns for SYMBOL, DESCRIPTION, and REVISION.

LEGEND table with columns for SYMBOL, DESCRIPTION, and REVISION.

SEQUENCE OF CONSTRUCTION table with columns for NO., REVISION, and DATE.

SEQUENCE OF CONSTRUCTION table with columns for NO., REVISION, and DATE.

SEQUENCE OF CONSTRUCTION table with columns for NO., REVISION, and DATE.

SEQUENCE OF CONSTRUCTION table with columns for NO., REVISION, and DATE.

SEQUENCE OF CONSTRUCTION table with columns for NO., REVISION, and DATE.

SEDIMENT CONTROL NOTES

SEDIMENT CONTROL NOTES
